

CITY OF LARKSPUR  
**Bon Air Bridge  
Replacement Project**



**JUNE-JULY 2019**

*Additional project information is available on the project website and comments or questions about the project can be directed to the Project Infoline or Project Email address listed below.*

**PROJECT INFOLINE:**  
**(415) 524-4500**


**PROJECT EMAIL:**  
[info@bonairbridge.com](mailto:info@bonairbridge.com)

**PROJECT WEBSITE:**  
[www.bonairbridge.com](http://www.bonairbridge.com)

**PUBLIC NOTICE OF CONSTRUCTION**

**JUNE-JULY 2019: STAGE 1 BRIDGE CONSTRUCTION WORK CONTINUES**

**Pier 2 Bent Cap Installation**

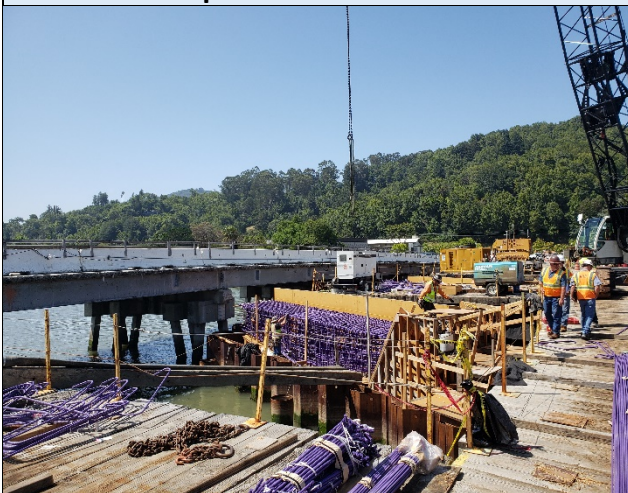

**30-inch RCP Storm Drain Pipe Installation**



**CONSTRUCTION UPDATE: JUNE-JULY 2019**

Construction work continues on Stage 1 bridge piers and bent caps with forming, placing reinforcement and concrete. The next step is concrete curing and form work removal. These activities are scheduled through the end of July. Roadwork improvements have started on Bon Air Road and will continue as we install underground drainage systems and PG&E utility relocations. Once the utility relocation work is complete (anticipated in late-July), roadwork will resume at the intersection of Bon Air and Magnolia Ave. We appreciate your patience and cooperation as we continue to make these important improvements.

**UPCOMING WORK: AUGUST-SEPTEMBER 2019\***

Early-August – Bon Air / Magnolia Intersection Roadwork Resumes

Mid-August – Installation of Precast Concrete Girders (Involves full road closures)

*\*Please note all dates are estimated and subject to change.*

**Next Steps:** Check the project website at [www.bonairbridge.com](http://www.bonairbridge.com) for updates on construction activities and project milestones.
